


Construction Areas: The following areas will be reconstructed in 2011:

- Highway 44 between Ewing Street and NE Circle Drive
- Portions of NE Main, NE and SE Jacob, NE Harvey, and Trailridge Road
- Work to begin April 11 and shall be 60 working days in length
- Construction to be completed in three phases




Phase 1 Staging:

- Construction shall be completed on Main Street and Trailridge Drive
- Work involves removing and replacing concrete pavement, water main, and sanitary sewer facilities; and constructing new storm sewer intakes
- Work to begin April 11 and shall be 15 working days in length
- Highway 44 open to traffic in both directions

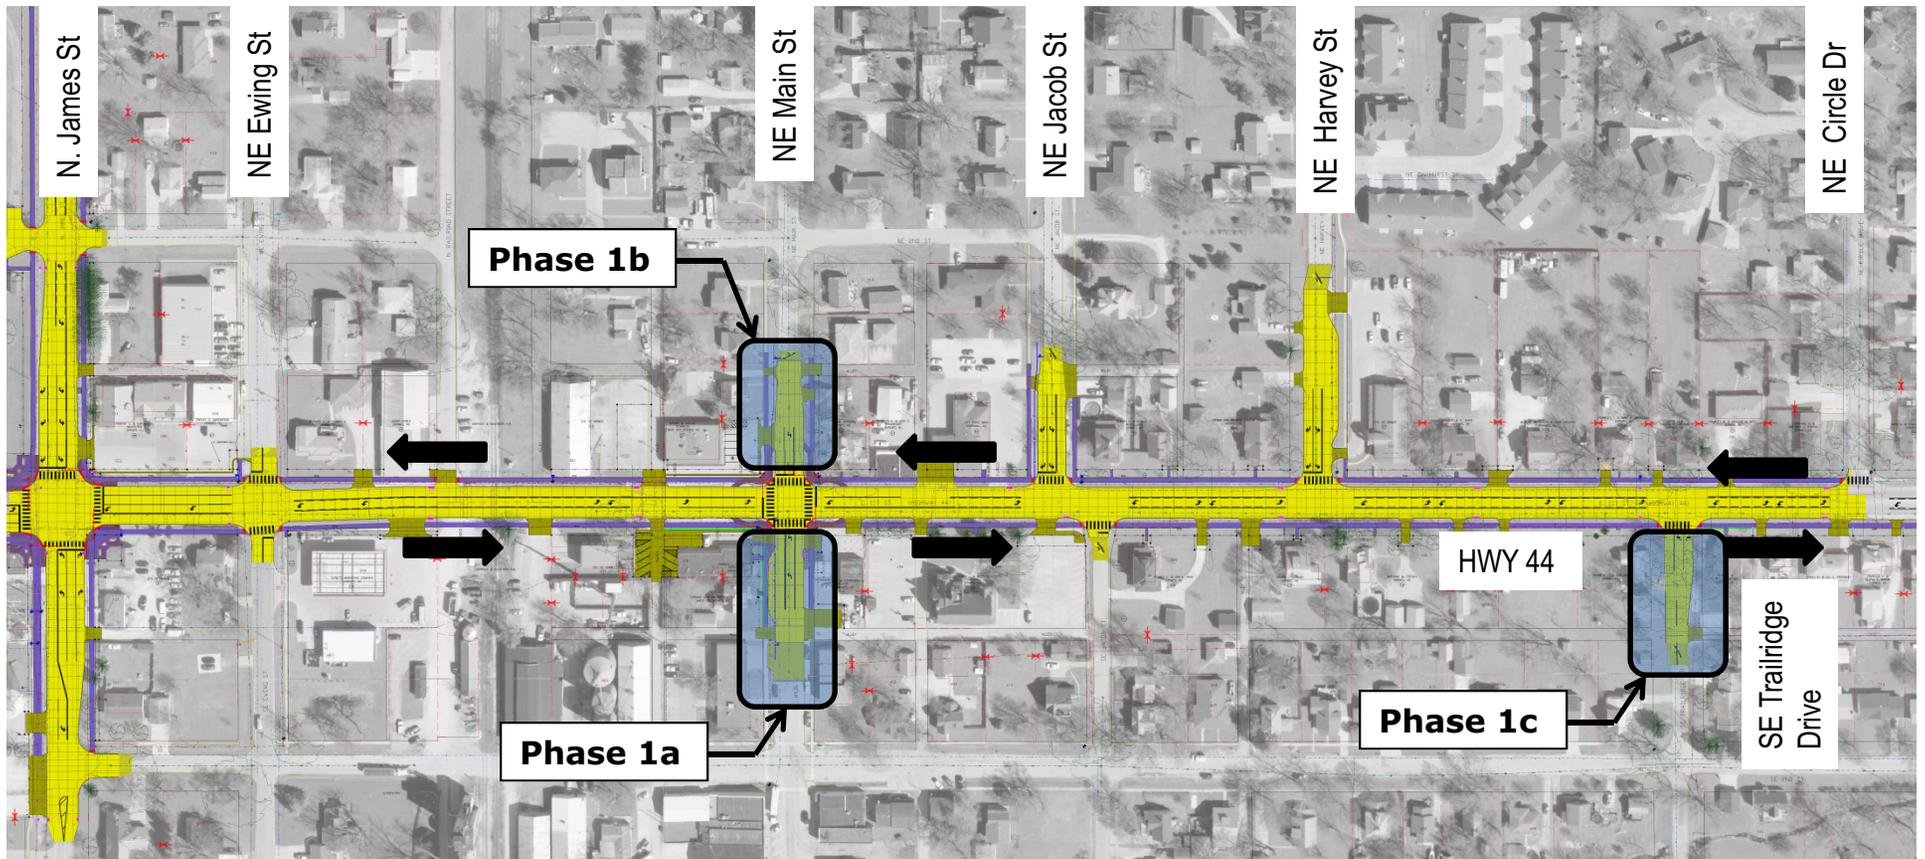

Phase 2 Staging:

- Construction shall be completed on NE Jacob and NE Harvey Streets; and the south (eastbound) lane of Highway 44
- Work involves removing and replacing concrete pavement, water main, and sanitary sewer facilities; and constructing new storm sewer intakes
- Work to begin April 26 and shall be 31 working days in length
- Highway 44 open to westbound traffic on existing north lane
- Eastbound Highway 44 traffic to detour along SE 19<sup>th</sup> Street

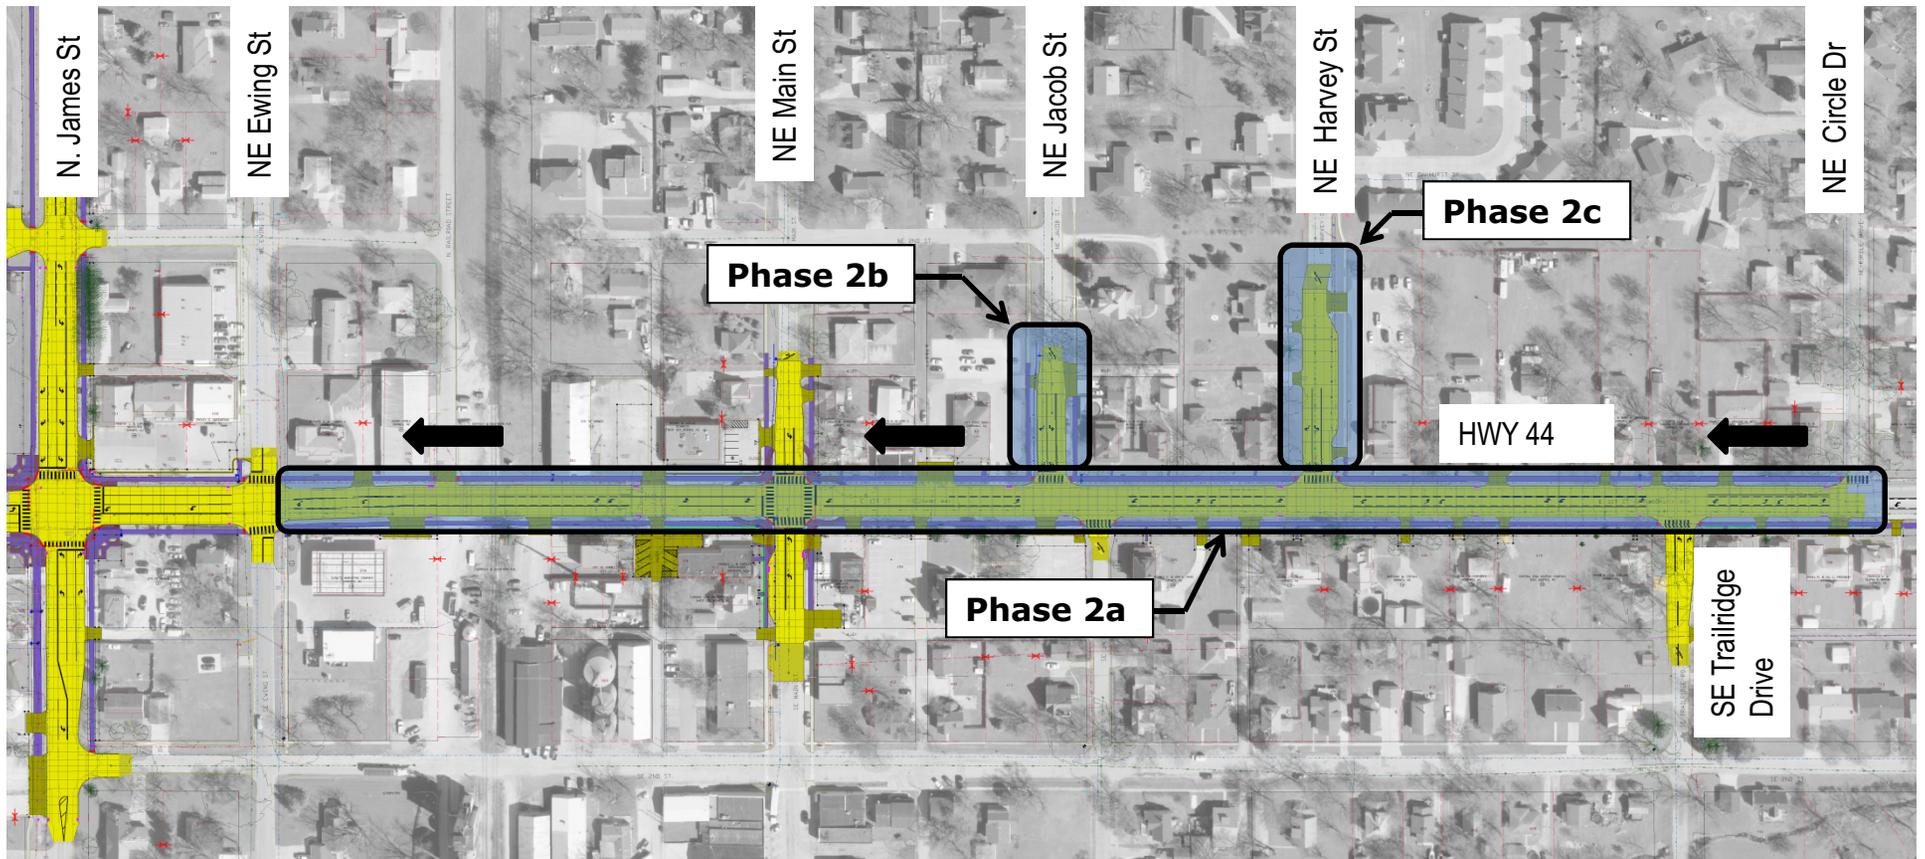

Phase 3 Staging:

- Construction shall be completed on the north (westbound) lane of Highway 44
- Work involves removing and replacing concrete pavement, water main, and sanitary sewer facilities; and constructing new storm sewer intakes
- Work to begin June 8 and shall be 32 working day in length
- Highway 44 open to westbound traffic on new south lane
- Eastbound Highway 44 traffic to detour along SE 19<sup>th</sup> Street

